BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads and Drains at Chanukya Layout Right side in Ward No. 06 Thainsandra Village Limit	
2	Estimate Cost	40.00 Lakhs	
3	Administrative Approved No and Date	538/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	130/13-14, Ddate. 23.12.2013	
5	Job Code No. and P Code No.	006-14-000076	
6	Tender Direct Entrested to KRIDL	Nil	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	18/2013-14, Date. 13.01.2014	
8	Tender Approved Details	Tender Approved by Chief Engineer Yelahanka Zone and Joint Commissioner Yelahanka Zone Wide Note Sheet para no.14	
9	Work Order No and Date	520/13-14, Date. 24.02.2014	
10	Stipulation time of Completion	60 Days	
11	Actiual Date of Commencement	01.03.2014	
12	Actiual Date of Completion	30.04.2014	
13	Delay if any	Nil	

14	Reason for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	01.07.2015	
19	MB No. and Page No.	Mb No.8907 Page No. 190612-621	
20	BR No. and Date	06/30.04.2014	
21	Test Result	Quality Test Report submitted by Civil Tech Consultents and Engineers is verified and Enclosed	
22	Section officer	Sri K Devegowda J.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	

Executive Engineer
Byatarayanapura Division
Yalahanka Zone, B.B.M.P.
Bangalore-560092

1/7/15

Y C Kale gowda
Executive Engineer (Retd)

- Improvements to Roads and Drains at Chanukya Layout Right side in Ward No. 06

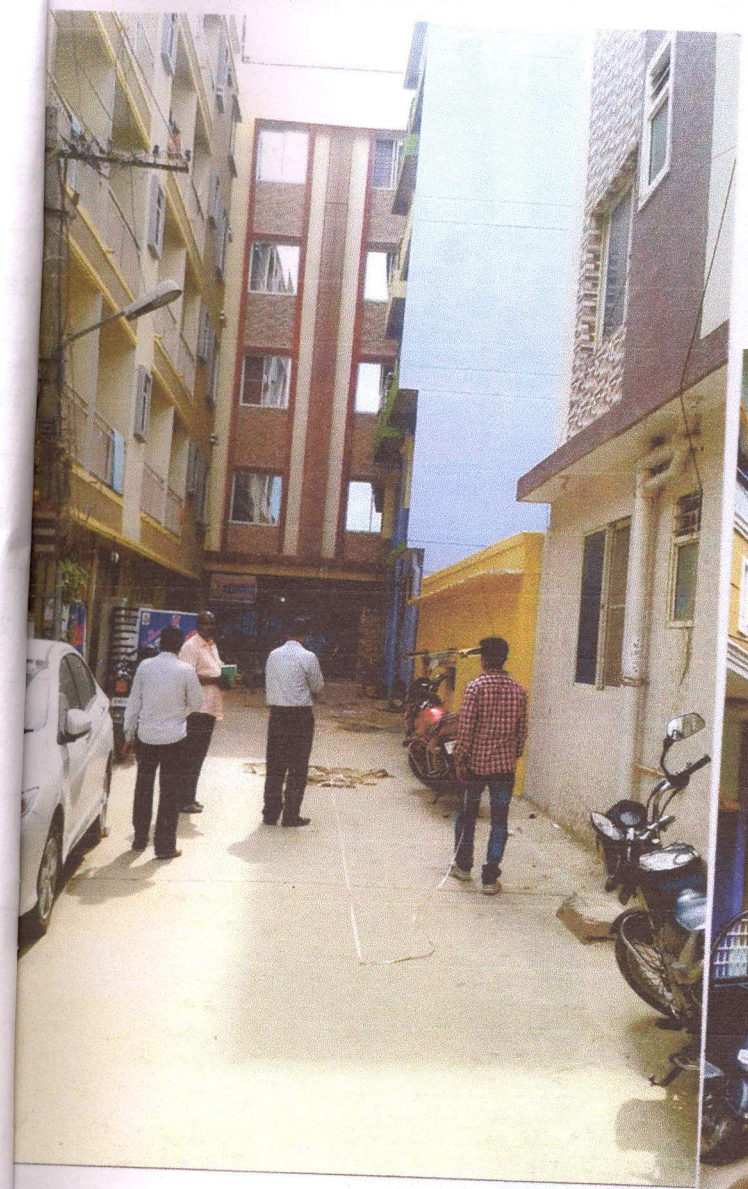

- Improvements to Roads and Draing at Chanukya Layout Right Side in Ward No-06

Improvements to Roads and Drains at Chanukya Layout Right Side in Ward no-06
